

Memorandum



CITY OF DALLAS

DATE April 13, 2026

Honorable Members of the Public Safety Committee
TO Cara Mendelsohn (Chair), Jesse Moreno (Vice Chair), Laura Cadena, Maxie Johnson,
Jaime Resendez, William Roth, Kathy Stewart

SUBJECT **Fire Station Alerting System Implementation**

Please accept this memorandum as an update on the ongoing installation of the Fire Station Alerting System project involving Dallas Fire-Rescue (DFR), in collaboration with Facilities and Real Estate Management (FRM), Information & Technology Services (ITS), and Honeywell International Inc. through its US Digital Designs Group.

BACKGROUND

The Fire Station Alerting System was approved on the City Council's December 11th, 2024, agenda as item #24-3630. The Fire Station Alerting System project launched with a kickoff meeting on March 26, 2025. Honeywell subcontractor deployed additional installers, and progress is ahead of schedule. Nine of thirteen stations in Battalions 1 and 2 are complete. Project completion remains targeted for February 2027, with opportunities to accelerate under review with Honeywell.

Current Progress:

- Installations complete: 9 of 13 (pending final inspections)
 - Battalion 1 (3,6,4,18,24, & 45)
 - Battalion 2 (2,7, & 20)
- In progress:
 - Station 10 (62%)
 - Station 56 (98%)
 - Stations 13 (5%)
 - Station 21 (5%) **Battalion 7**

Asbestos survey reports for Battalions 1, 2, 3, and 4 have been finalized, and mitigation activities are underway

Timeline:


Project – Schedule Overview

Financial Summary

Total Budget: \$4,567,164
 Remaining Budget: \$3,210,464



Program Timeline

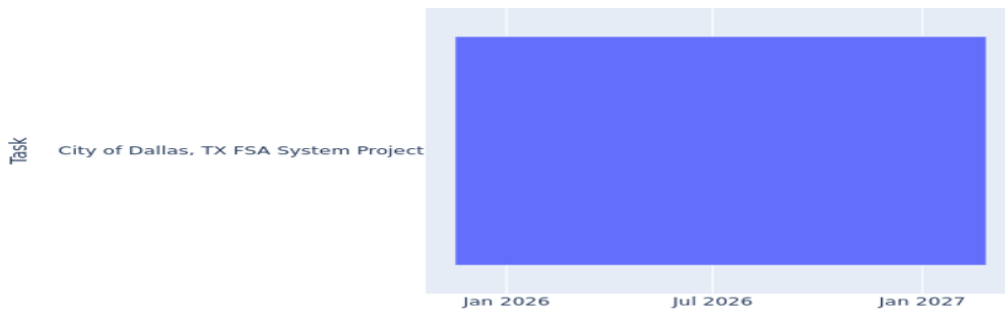


Task	Start	Finish	Percent
City of Dallas, TX FSA System Project	2025-11-17	2027-02-26	28%

Battalion 2 – Schedule Overview


STATUS

Battalion 2 Timeline

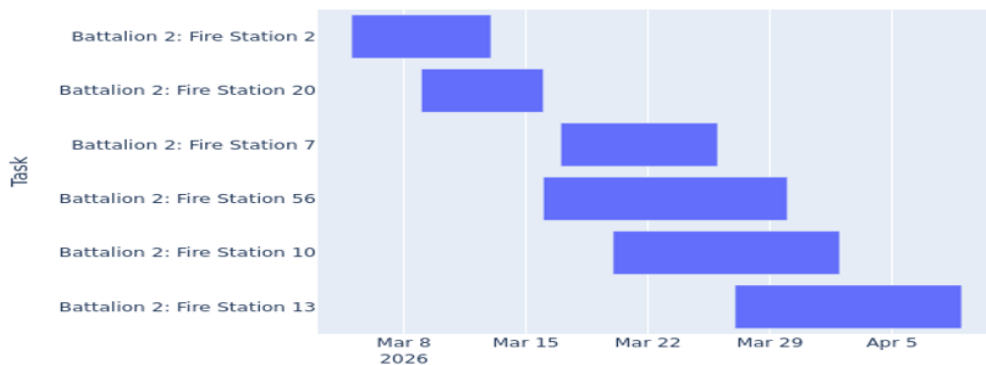


Task	Start	Finish	Percent
Battalion 2: Fire Station 2	2026-03-05	2026-03-13	100%
Battalion 2: Fire Station 20	2026-03-09	2026-03-16	100%
Battalion 2: Fire Station 7	2026-03-17	2026-03-26	100%
Battalion 2: Fire Station 56	2026-03-16	2026-03-30	98%
Battalion 2: Fire Station 10	2026-03-20	2026-04-02	62%
Battalion 2: Fire Station 13	2026-03-27	2026-04-09	5%

Battalion 3 – Schedule Overview

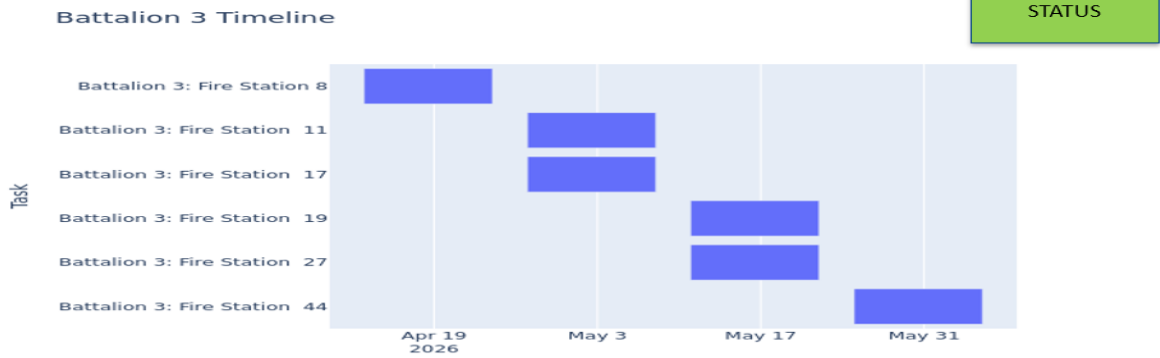

Task	Start	Finish	Percent
Battalion 3: Fire Station 8	2026-04-13	2026-04-24	0%
Battalion 3: Fire Station 11	2026-04-27	2026-05-08	0%
Battalion 3: Fire Station 17	2026-04-27	2026-05-08	0%
Battalion 3: Fire Station 19	2026-05-11	2026-05-22	0%
Battalion 3: Fire Station 27	2026-05-11	2026-05-22	0%
Battalion 3: Fire Station 44	2026-05-25	2026-06-05	0%

Battalion 7: Station 21 – Schedule Overview

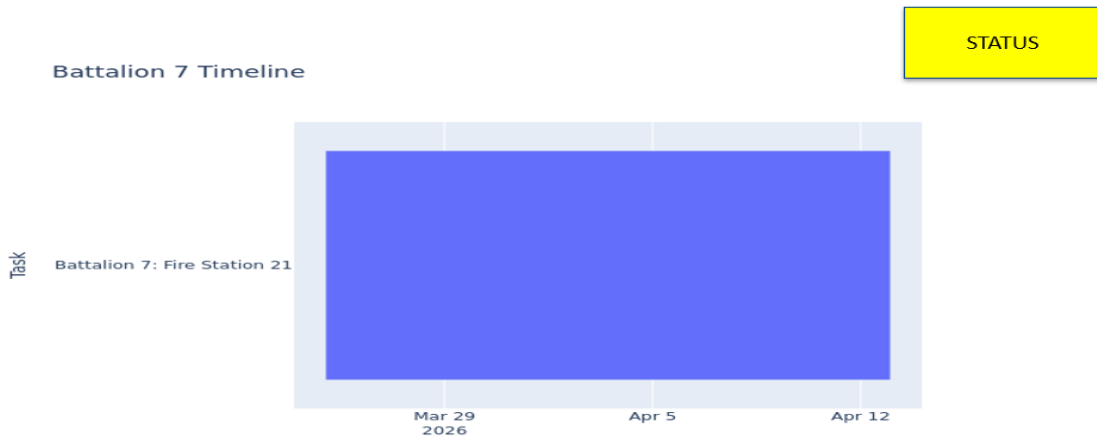

Task	Start	Finish	Percent
Battalion 7: Fire Station 21	2026-03-25	2026-04-13	5%

Issues & Risks

- No Wire or Pathway at FS21 for Honeywell FSA system installs| Delays installation until pathway is established| Mitigation: Coordinating with AVI & construction contractor to resolve issue

DATE April 13, 2026
SUBJECT **Fire Station Alerting System Implementation**
PAGE **4 of 4**

Next Battalion Timeline: April – June 2026

Battalion 3

April 13 – April 24, 2026

- Station 8

April 27 – May 8, 2026

- Station 11
- Station 17

May 11 – May 22, 2026


- Station 19
- Station 27

May 26 – June 6, 2026

- Station 44
- Station 22 (**Battalion 4**)

Should you have questions or concerns, please contact Fire Chief Justin Ball at justin.ball@dallasfire.gov.

Service First, Now!



Dominique Artis

Chief of Public Safety

cc: Kimberly Bizzor Tolbert, City Manager
Tammy Palomino, City Attorney
Mamatha Sparks, City Auditor (I)
Biliera Johnson, City Secretary
Preston Robinson, Administrative Judge
Baron Eliason, Inspector General (I)
Dev Rastogi, Assistant City Manager

M. Elizabeth (Liz) Cedillo-Pereira, Assistant City Manager
Alina Ciocan, Assistant City Manager
Donzell Gipson, Assistant City Manager
Robin Bentley, Assistant City Manager
Jack Ireland, Chief Financial Officer
Ahmad Goree, Chief of Staff to the City Manager
Directors and Assistant Directors
