

Memorandum



CITY OF DALLAS

DATE May 11, 2026

Honorable Members of the Public Safety Committee

TO Cara Mendelsohn (Chair), Jesse Moreno (Vice Chair), Laura Cadena, Maxie Johnson, Jaime Resendez, William Roth, Kathy Stewart

SUBJECT **Fire Station Alerting System Implementation Update**

Please accept this memorandum as an update on the ongoing installation of the Fire Station Alerting System project involving Dallas Fire-Rescue (DFR), in collaboration with Facilities and Real Estate Management (FRM), Information & Technology Services (ITS), and Honeywell International Inc. through its US Digital Designs Group.

BACKGROUND



The Fire Station Alerting System was approved by the City Council on the December 11, 2024, agenda as item #24-3630. The Fire Station Alerting System project launched with a kickoff meeting on March 26, 2025. Honeywell subcontractor deployed additional installers, and progress is ahead of schedule. Thirteen of nineteen stations in Battalions 1, 2, and 3 are complete. Project completion remains targeted for February 2027, with opportunities to accelerate under review with Honeywell.

Current Progress:


- Installations complete: 14 of 19 (pending final inspections)
 - Battalion 1 (3,6,4,18,24, & 45)
 - Battalion 2 (2,7,10,13, 20)
 - Battalion 3 (8, and 11)
- In progress:
 - Station 56 (98%) **Battalion 2**
 - Station 21 (70%) **Battalion 7**
 - Station 17 (0%)
 - Station 19 (60%)
 - Station 27 (0%)
 - Station 44 (20%)

Asbestos survey reports for Battalions 1, 2, 3, and 4 have been finalized, and mitigation activities are underway


Project Timeline:

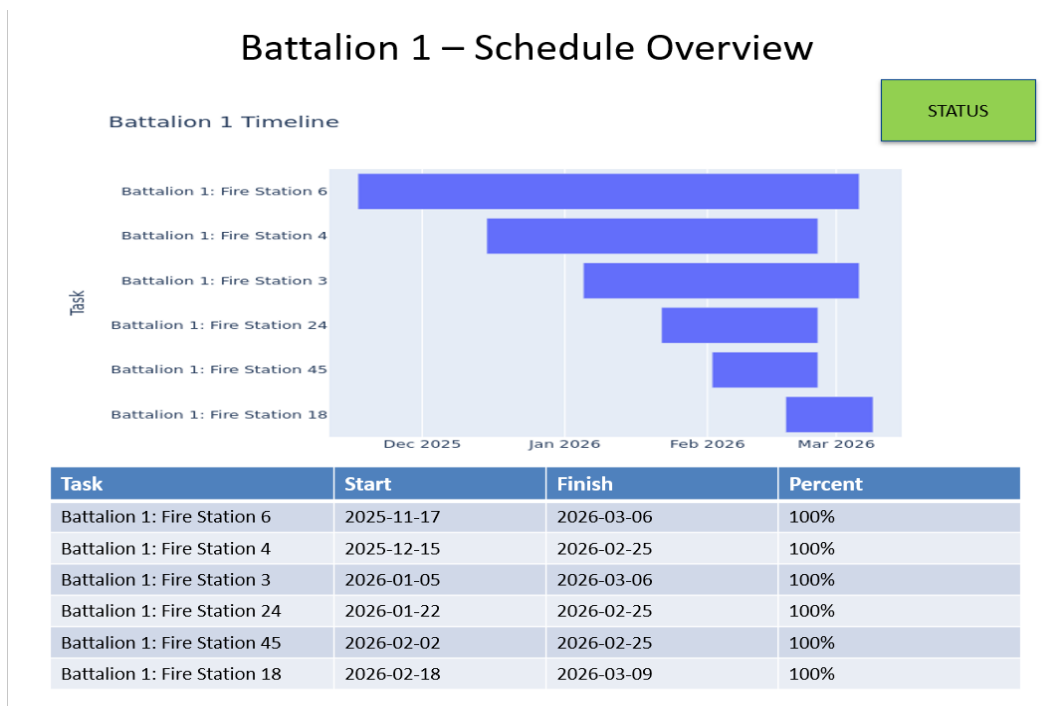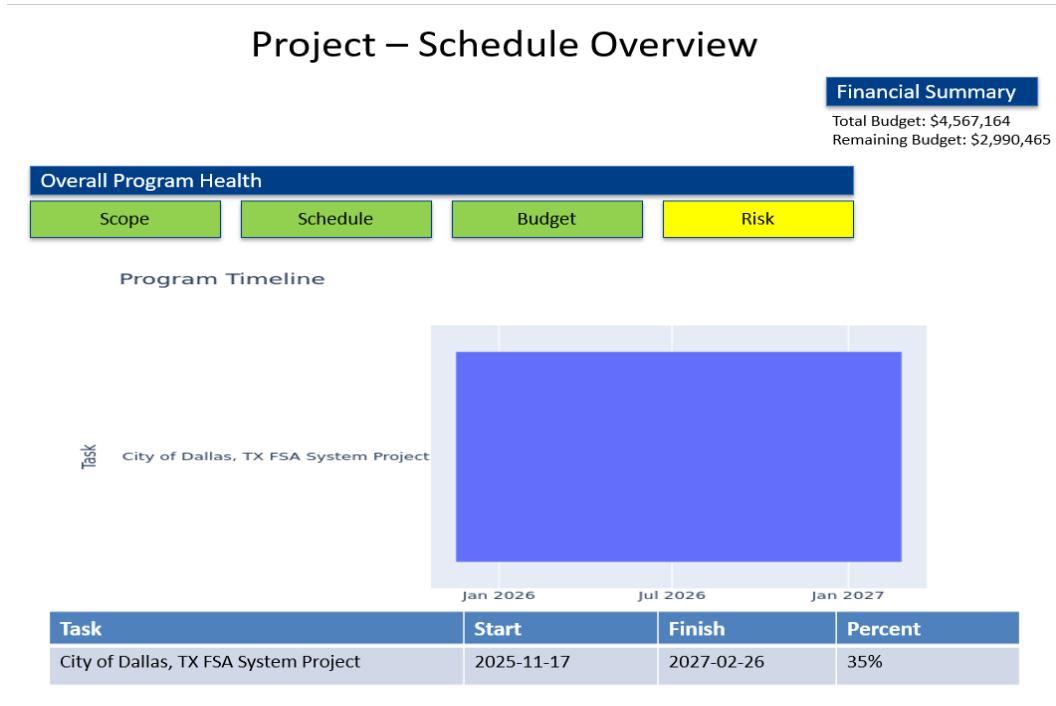


Battalion 2 – Schedule Overview

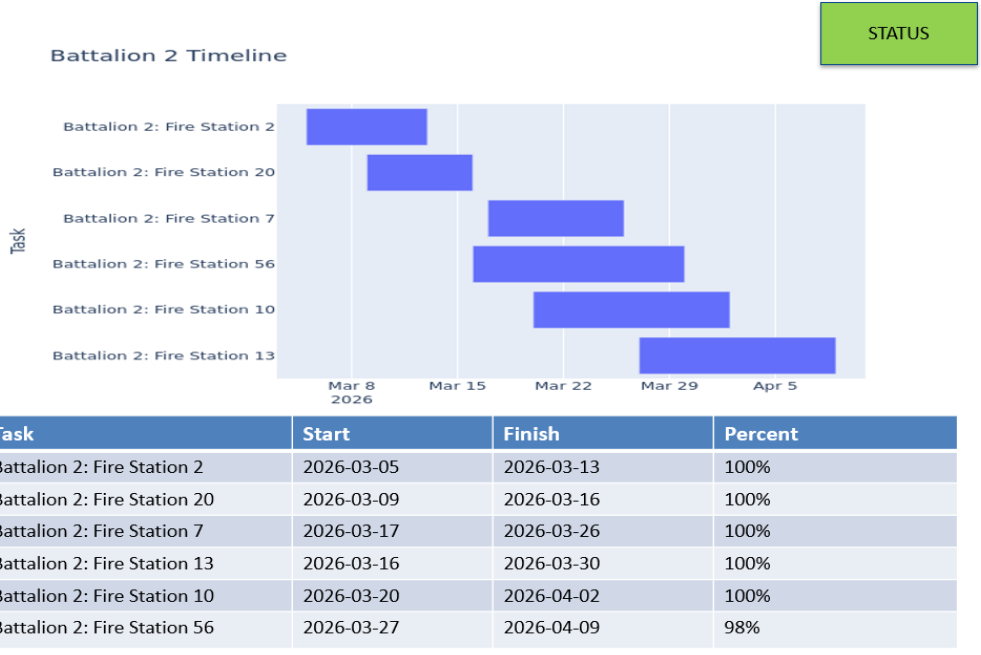

Battalion 3 – Schedule Overview

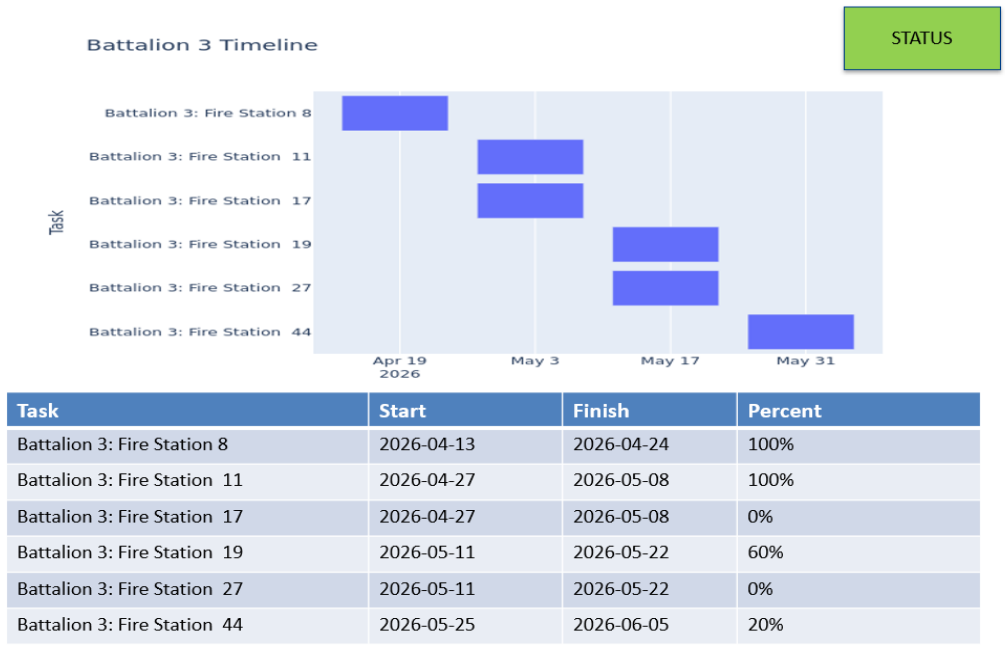

Battalion 7: Station 21 – Schedule Overview

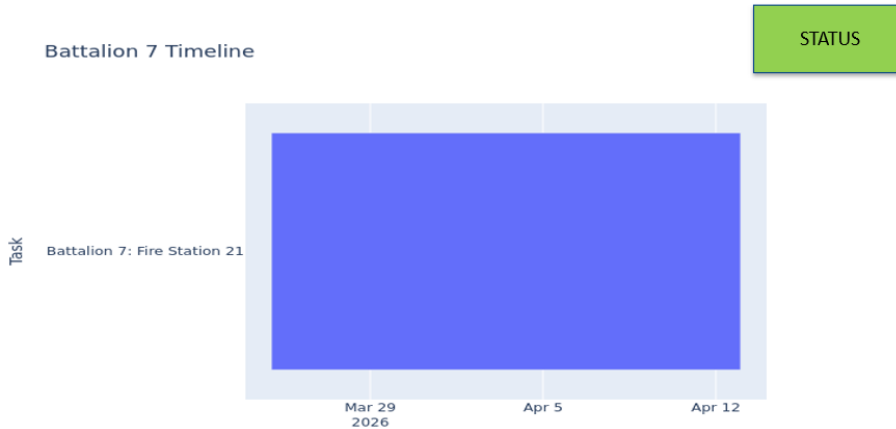

Task	Start	Finish	Percent
Battalion 7: Fire Station 21	2026-03-25	2026-05-01	70%

Issues & Risks

- No Wire or Pathway at FS21 for Honeywell FSA system installs | Delays installation until pathway is established |
Mitigation: A change order has been approved for the Honeywell sub-contractor to install the required cabling and create the necessary pathway.

Next Battalion Timeline: April - June

Battalion 3

April 13 – April 24

- Station 8

April 27 – May 8

- Station 11
- Station 17

May 11 – May 22

- Station 19
- Station 27


May 26 – June 6

- Station 44
- Station 22 (**Battalion 4**)

DATE April 27, 2026
SUBJECT **Fire Station Alerting System Implementation Update**
PAGE **2 of 5**

Should you have any question or concerns, please contact Fire Chief Justin Ball at justin.ball@dallasfire.gov

Service First, Now!



Dominique Artis
Chief of Public Safety

c: Kimberly Bizer Tolbert, City Manager
Bertram Vandenberg, City Attorney (I)
Mamatha Sparks, City Auditor (I)
Billierae Johnson, City Secretary
Preston Robinson, Administrative Judge
Baron Eliason, Inspector General (I)

Dev Rastogi, Assistant City Manager
M. Elizabeth (Liz) Cedillo-Pereira, Assistant City Manager
Alina Ciocan, Assistant City Manager
Robin Bentley, Assistant City Manager
Jack Ireland, Chief Financial Officer
Ahmad Goree, Chief of Staff to the City Manager
John Johnson, Chief of Real Estate
Directors and Assistant Directors
