

Memorandum



DATE June 8, 2026

CITY OF DALLAS

Honorable Members of the Public Safety Committee
TO Cara Mendelsohn (Chair), Jesse Moreno (Vice Chair), Laura Cadena, Maxie Johnson,
Jaime Resendez, William Roth, Kathy Stewart

SUBJECT **Fire Station Alerting System Implementation Update**

Please accept this memorandum as an update on the ongoing installation of the Fire Station Alerting System project involving Dallas Fire-Rescue (DFR), in collaboration with Facilities and Real Estate Management (FRM), Information & Technology Services (ITS), and Honeywell International Inc. through its US Digital Designs Group.

BACKGROUND

The Fire Station Alerting System, approved by the City Council on December 11, 2024 (agenda item #24-3630), officially began implementation with a project kickoff on March 26, 2025. Since launch, installation of the new alerting technology has been completed at sixteen of the fifty-nine fire stations included in the project scope.

Current Progress:

The project is currently performing ahead of plan, running eight days ahead of schedule, with installation at Battalion 4 initiated on May 18, 2026. Several stations remain on hold, pending equipment shipments and completion of required abatement. To mitigate these delays, the installation vendor has adjusted the sequence of work to continue progress while awaiting materials and site clearance.

Overall completion remains on track for the targeted February 2027 finish date. In partnership with Honeywell, the project team is also evaluating opportunities to further accelerate deployment while maintaining quality and operational readiness

- Installation complete: 16 of 59 stations
 - Battalion 1 (3,6,4,18,24, and 45)
 - Battalion 2 (2,7,10,13, 20)
 - Battalion 3 (8,11,19,27 and 44)
- In progress:
 - Station 56 (98%) **Battalion 2**
 - Station 28 (48%) **Battalion 4**
 - Station 21 (70%) **Battalion 7**
 - Station 17 (0%) Waiting for abatement estimated completion May 30, 2026.

Asbestos survey reports for Battalions 1, 2, 3, and 4 have been finalized, and mitigation activities are underway.

Next Battalion Timeline: April – June:


Project – Schedule Overview

Financial Summary

Total Budget: \$4,567,164
 Remaining Budget: \$2,736,438




Program Timeline

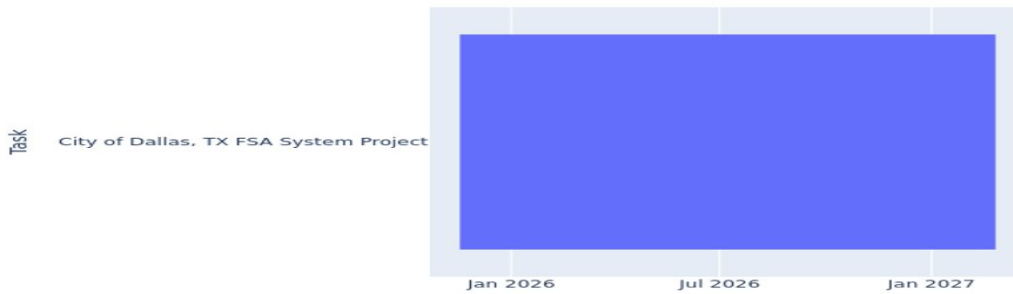


Task	Start	Finish	Percent
City of Dallas, TX FSA System Project	2025-11-17	2027-02-26	35%

Battalion 1 – Schedule Overview

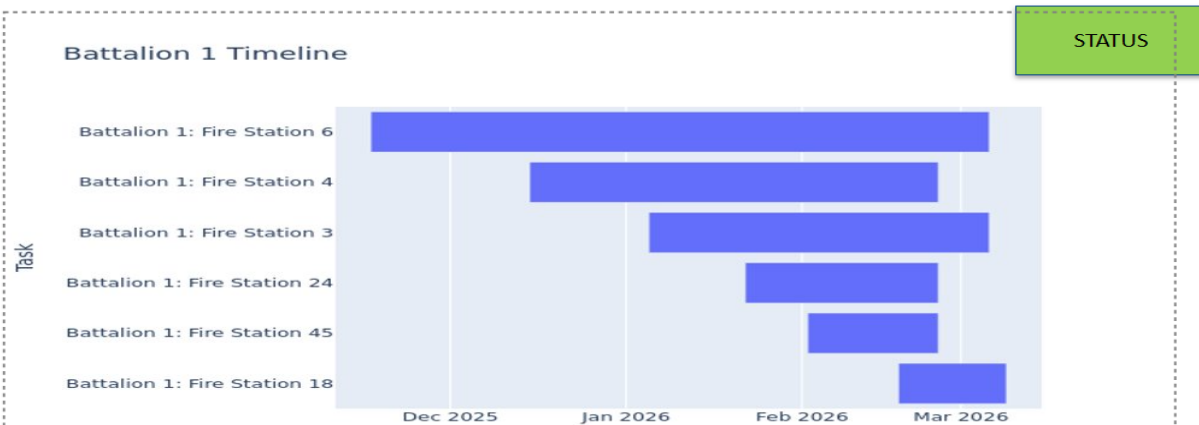


Task	Start	Finish	Percent
Battalion 1: Fire Station 6	2025-11-17	2026-03-06	100%
Battalion 1: Fire Station 4	2025-12-15	2026-02-25	100%
Battalion 1: Fire Station 3	2026-01-05	2026-03-06	100%
Battalion 1: Fire Station 24	2026-01-22	2026-02-25	100%
Battalion 1: Fire Station 45	2026-02-02	2026-02-25	100%
Battalion 1: Fire Station 18	2026-02-18	2026-03-09	100%

Battalion 2 – Schedule Overview

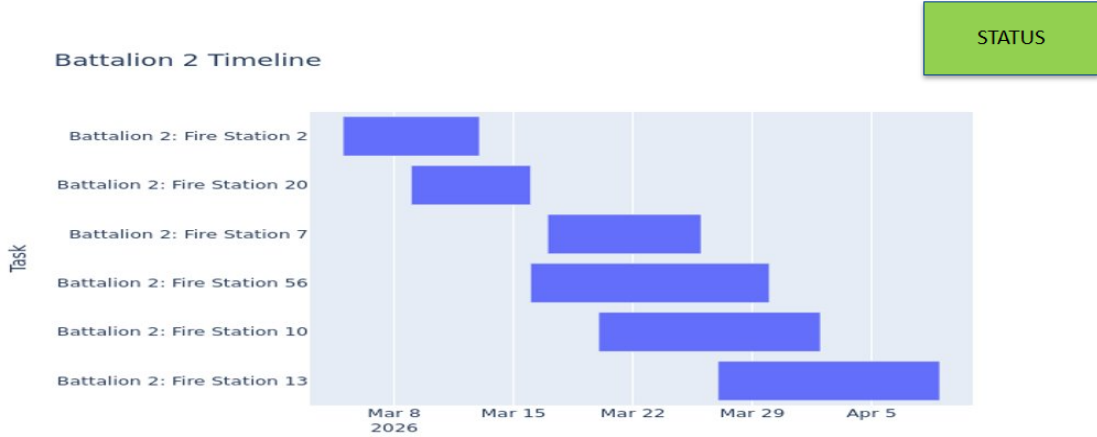

Task	Start	Finish	Percent
Battalion 2: Fire Station 2	2026-03-05	2026-03-13	100%
Battalion 2: Fire Station 20	2026-03-09	2026-03-16	100%
Battalion 2: Fire Station 7	2026-03-17	2026-03-26	100%
Battalion 2: Fire Station 13	2026-03-16	2026-03-30	100%
Battalion 2: Fire Station 10	2026-03-20	2026-04-02	100%
Battalion 2: Fire Station 56	2026-03-27	2026-04-09	98% awaiting equipment from USDD


Battalion 7: Station 21 – Schedule Overview

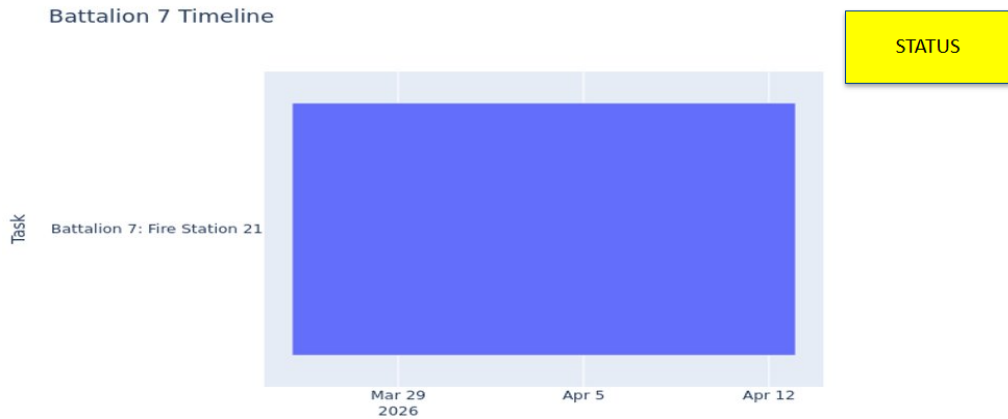

Task	Start	Finish	Percent
Battalion 7: Fire Station 21	2026-03-25	2026-05-01	70% waiting on an outdoor speaker and discussing penetration methods with the GC representative

Issues & Risks

- No Wire or Pathway at FS21 for Honeywell FSA system installs| Delays installation until pathway is established |
Mitigation: A change order has been approved for the Honeywell sub-contractor to install the required cabling and create the necessary pathway.

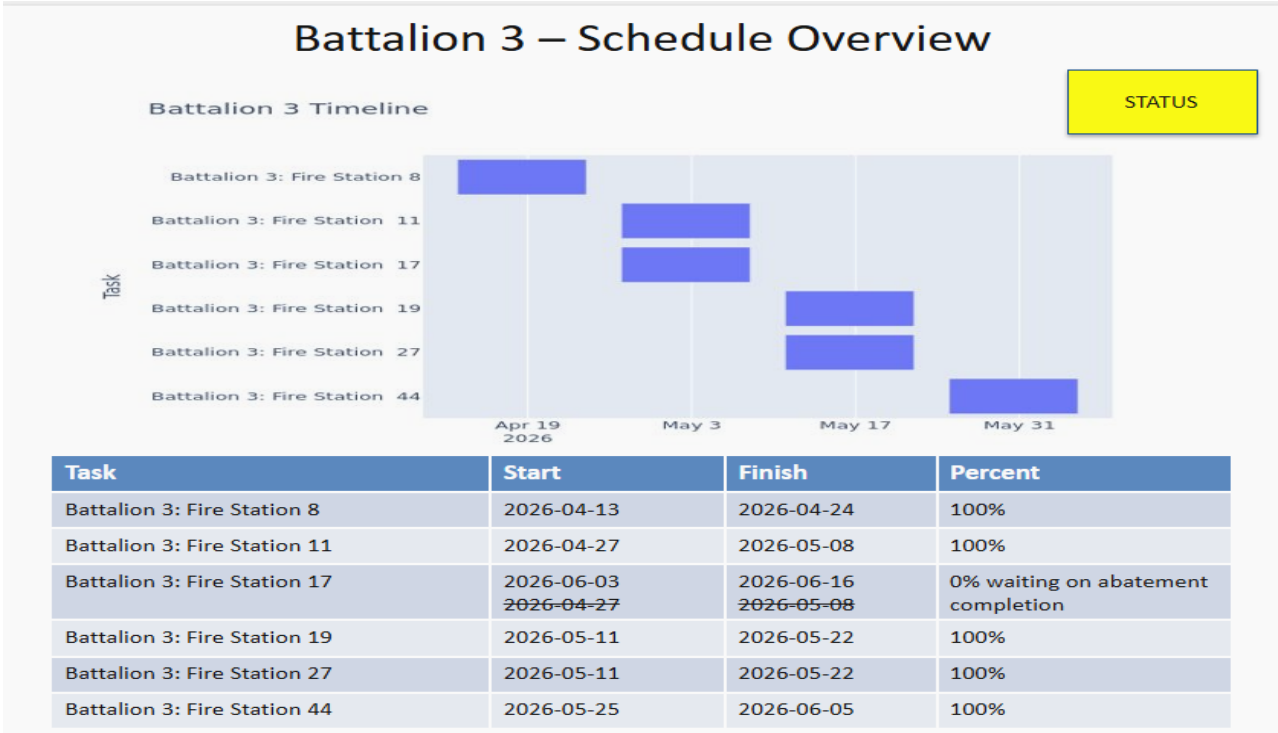

Installation Dates:

Battalion 3

April 13 – April 24

- Station 8

April 27 – May 8

- Station 11
- Station 17

May 11 – May 22

- Station 19
- Station 27

May 26 – June 6

- Station 44

Battalion 4

May 18 – Jun 02

- Station 28 (48%)

DATE June 8, 2026
SUBJECT **Fire Station Alerting System Implementation Update**
PAGE **5 of 5**

- Station 37

Jun 03 – June 26

- Station 17
- Station 29
- Station 41

Jun 22 – July 17

- Station 22
- Station 57

Should you have any question or concerns, please contact Fire Chief Justin Ball at justin.ball@dallasfire.gov

Service First, Now!



Dominique Artis
Chief of Public Safety

c: Kimberly Bizer Tolbert, City Manager
Bertram Vandenberg, City Attorney (I)
Mamatha Sparks, City Auditor (I)
Biliera Johnson, City Secretary
Preston Robinson, Administrative Judge
Baron Eliason, Inspector General (I)

Dev Rastogi, Assistant City Manager
M. Elizabeth (Liz) Cedillo-Pereira, Assistant City Manager
Alina Ciocan, Assistant City Manager
Robin Bentley, Assistant City Manager
Jack Ireland, Chief Financial Officer
Ahmad Goree, Chief of Staff to the City Manager
John Johnson, Chief of Real Estate
Directors and Assistant Directors
