

Memorandum



CITY OF DALLAS

DATE August 10, 2026

Honorable Members of the Public Safety Committee

TO Cara Mendelsohn (Chair), Jesse Moreno (Vice Chair), Laura Cadena, Maxie Johnson, Jaime Resendez, William Roth, Kathy Stewart

SUBJECT **Fire Station Alerting System Implementation Update**

Please accept this memorandum as an update on the ongoing installation of the Fire Station Alerting System project involving Dallas Fire-Rescue (DFR), in collaboration with Facilities and Real Estate Management (FRM), Information & Technology Services (ITS), and Honeywell International Inc. through its US Digital Designs Group.

BACKGROUND

The Fire Station Alerting System, approved by the City Council on December 11, 2024 (agenda item #24-3630), officially began implementation with a project kickoff on March 26, 2025. Since launch, installation of the new alerting technology has been completed at twenty-seven of the fifty-nine fire stations within the project scope.

Current Progress:

Overall completion remains on track for the targeted February 2027 finish date. The installation of the new Fire Station Alerting System continues to advance on schedule. To date, installation activities have been completed—pending final cutover—at 27 stations across Battalions 1, 2, 3, 4, 5, and at the new ARFF Station 21.

Abatement treatment is underway at select stations. To maintain schedule momentum and prevent delays, the installation team has proactively shifted work to other stations while abatement activities are in progress. This approach keeps the project on a positive trajectory and supports uninterrupted progress across the deployment.

Installation Progress:


Completed Installations (27 Stations – Pending Final Cutover)

- Battalion 1: Stations 3, 6, 4, 18, 24, 45
- Battalion 2: Stations 2, 7, 10, 13, 20, 56
- Battalion 3: Stations 8, 11, 17, 19, 27, 44
- Battalion 4: Stations 28, 29, 41, 37
- Battalion 5: Stations 25, 40, 46, 54
- Battalion 7: Station 21 (ARFF)


Active Installations

- Station 12 – 36% (In progress)
- Station 22 – 10% (In progress)
- Station 57 – 0% (Install site readiness)
- Station 49 – 0% (Install site readiness)


Next Battalion Timeline: July – August:

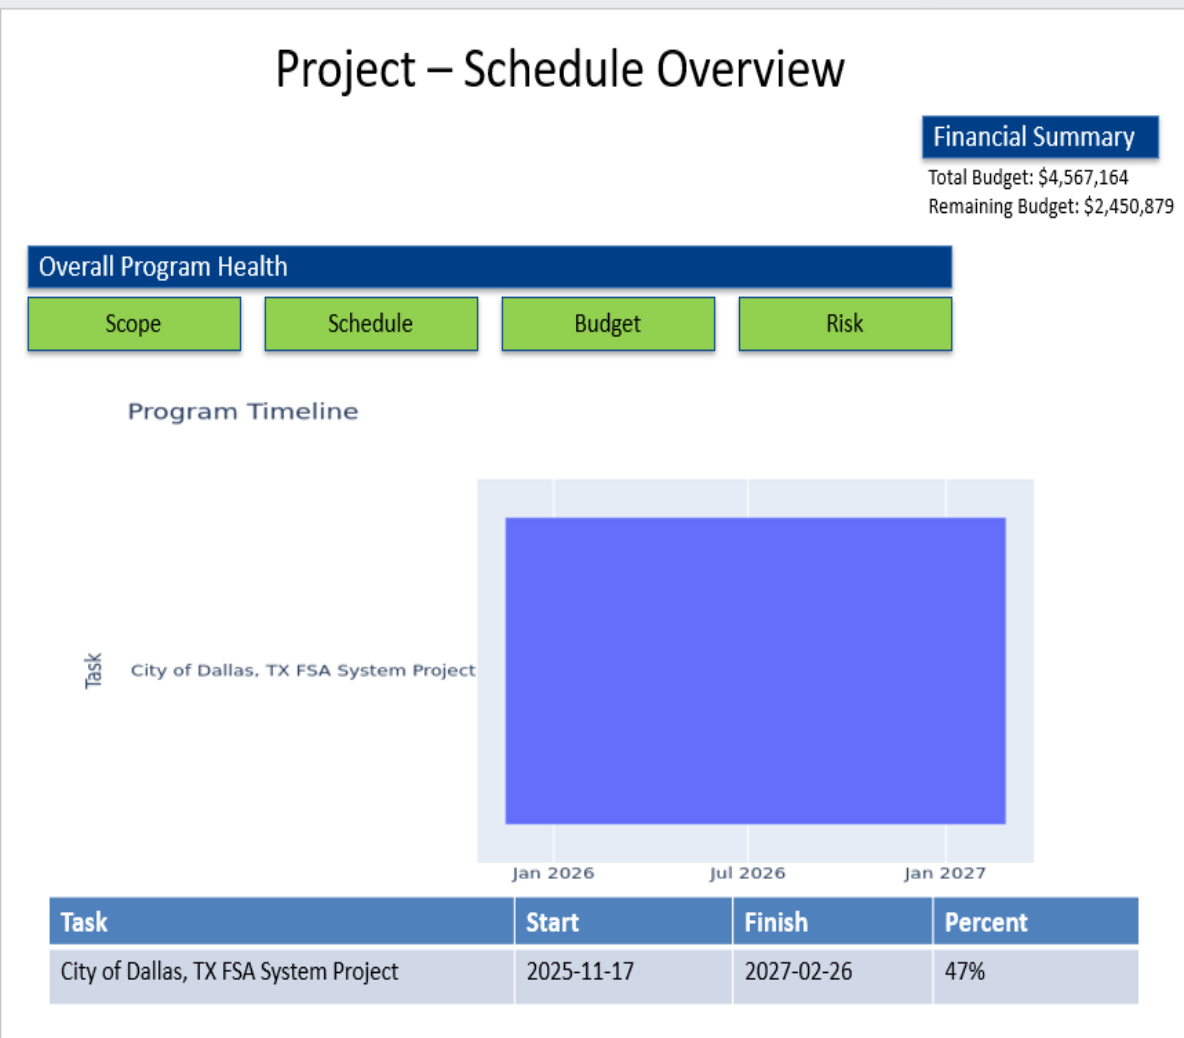


Battalion 4 – Schedule Overview

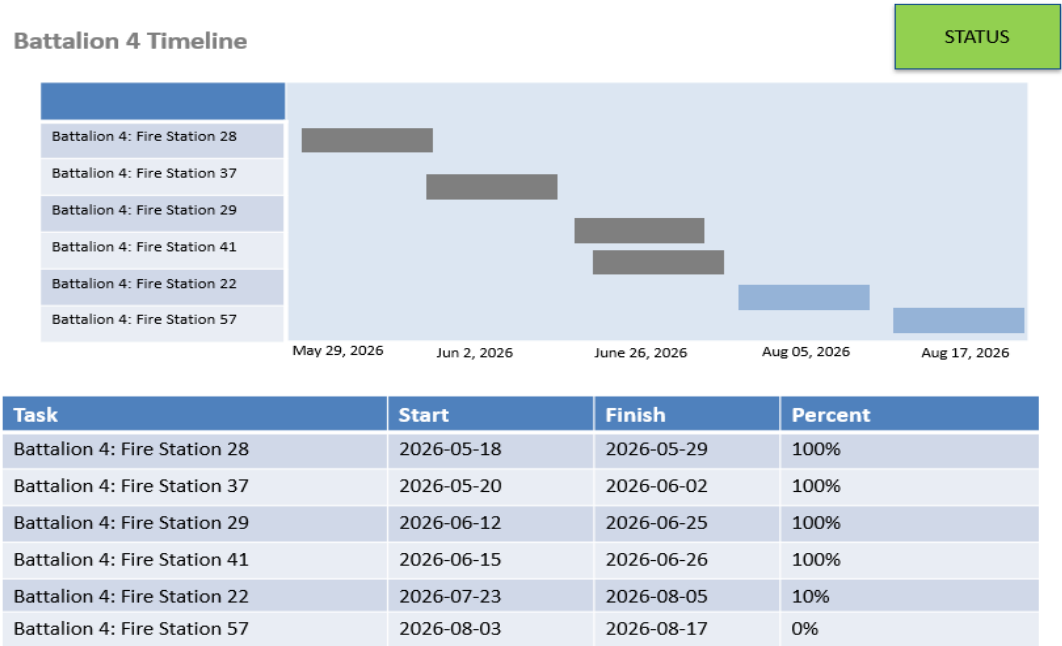

Battalion 5 – Schedule Overview

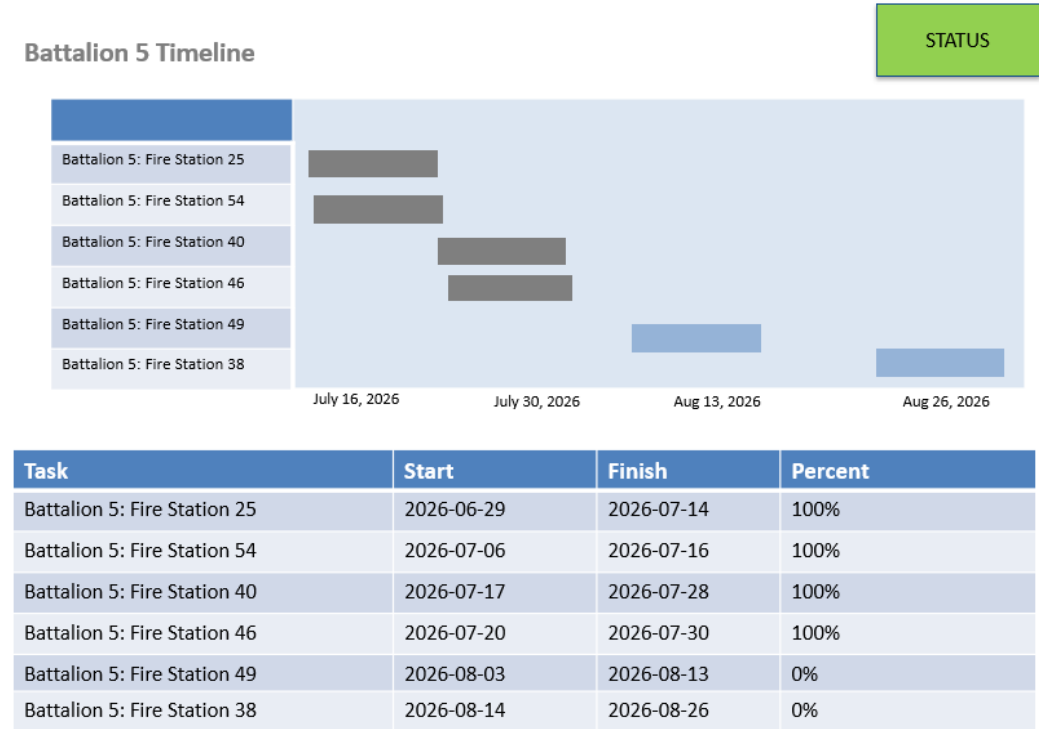

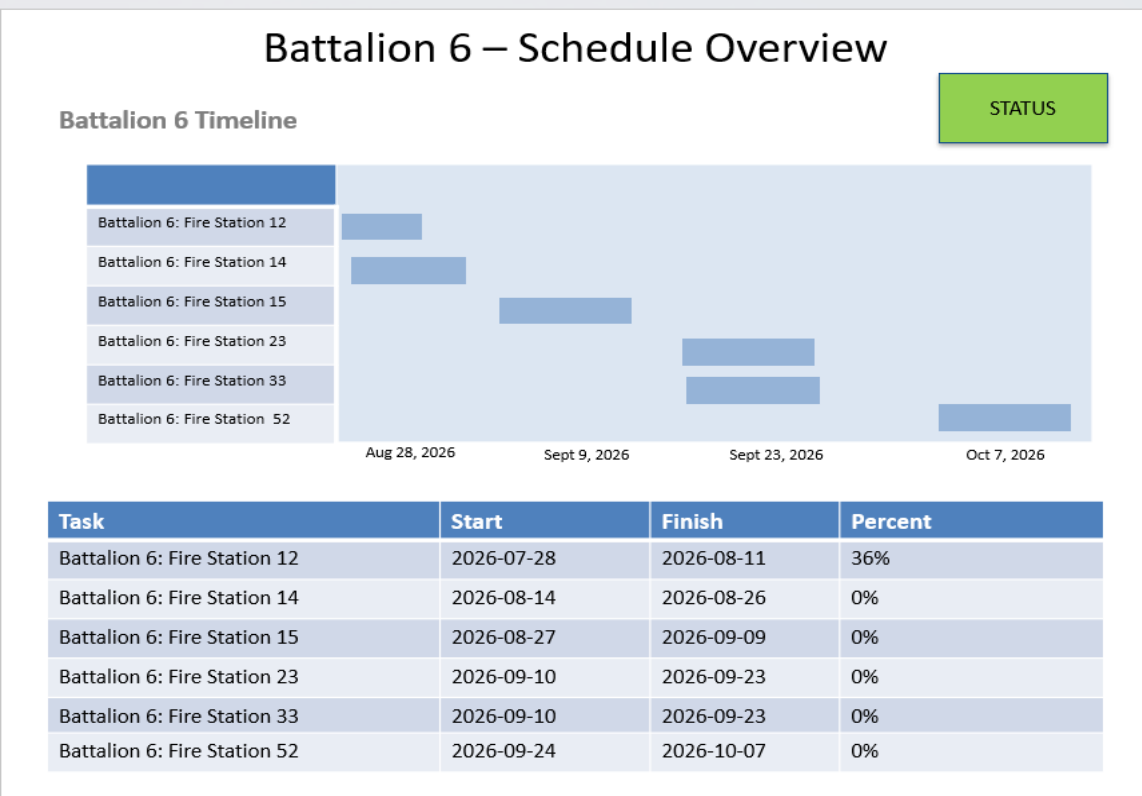

Should you have any question or concerns, please contact Fire Chief Justin Ball at justin.ball@dallasfire.gov

Service First, Now!

Dominique Artis
Chief of Public Safety

- c:

Kimberly Bizer Tolbert, City Manager

Bertram Vandenberg, City Attorney (I)

Mamatha Sparks, City Auditor (I)

Biliera Johnson, City Secretary

Preston Robinson, Administrative Judge

Baron Eliason, Inspector General (I)

Dev Rastogi, Assistant City Manager
- M. Elizabeth (Liz) Cedillo-Pereira, Assistant City Manager

Alina Ciocan, Assistant City Manager

Robin Bentley, Assistant City Manager

Jack Ireland, Chief Financial Officer

Ahmad Goree, Chief of Staff to the City Manager

John Johnson, Chief of Real Estate

Directors and Assistant Directors
